Execution plan

4.1 From strategy to initiatives

Twenty focus areas become eighteen initiatives, one per focus area except where one owner delivers two.

The plan follows one chain from vision to measure. Each level answers a different question. The pillar says what must change and the focus area says where; the initiative says what Wesgro and its partners do, and the indicator says how Steerco will know it has happened (section 5.1).

Table 4.1. Seven levels run from the vision to the measures, and each level has a fixed count in this plan.

Level	Count	What it answers	Example
Vision	1	Where the province is going	Grow international arrivals from 1.5m in 2025 toward 2.5m by 2035
Pillars	3	What must change	Reshape demand
Themes	6	In which part of the system	Source market growth and diversification
Focus areas	20	Where the evidence says to act	Convert India and China hub traffic
Initiatives	18	What Wesgro and its partners do	I4 India and China hub conversion
Actions	82	Who does what, by tier	Activate inside Xiaohongshu, Douyin and MakeMyTrip
Indicators	7, 25 and 36	How Steerco knows, at impact, outcome and output level	T2-06 India and China hub arrivals

Source: Chapter 3; traceability table, Appendix A1. Action count from the Chapter 3 action tables.

Two merges take twenty focus areas to eighteen initiatives. Segment-led marketing and mature-market yield share one owner and one set of channels, so focus areas 1 and 5 form initiative I1. Institutional alignment and industry collaboration share one forum, so focus areas 16 and 17 form I15. Every other focus area has its own initiative, numbered I1 to I18 in one sequence so that the M&E toolkit can track them on one list.

Leads are proposed, not agreed. They follow the Wesgro units named in the Inception Report's stakeholder map and the actions in Chapter 3, and Steerco confirms them at its first meeting [Steerco to confirm initiative leads and partners]. Six initiatives have a partner as the accountable lead, because the main lever sits outside Wesgro's mandate: corridor mobility, quality standards, flagship sites, community pilots, LTO funding and skills.

Table 4.2. Eighteen initiatives cover the twenty focus areas, and eleven of them are in implementation by 2028.

Code	Initiative	Focus areas	Proposed lead	Phase 1 role
I1	Segment-led activation and yield in mature markets	1, 5	Destination Marketing	Design, then implement
I2	Green-season events and business-events calendar	2	Convention Bureau	Design, then implement
I3	Bookable province programme	3	Tourism	Design, then implement
I4	India and China hub conversion	4	Destination Marketing	Design, then implement
I5	Regional Africa programme	6	Destination Marketing	Design, then implement

Code	Initiative	Focus areas	Proposed lead	Phase 1 role
I6	Route development and seat retention, with a public-private air access fund	7	Air Access	Implement
I7	Cruise growth through product	8	Cruise Cape Town	Design, then implement
I8	Corridor mobility	9	Department of Mobility, with Wesgro Tourism	Design
I9	Corridor product development	10	Tourism	Design
I10	Visitor experience and quality standards	11	DEDAT, with Wesgro Tourism	Design
I11	Flagship site demand management	12	Site operators, with Wesgro Research	Design
I12	Community inclusion pilots	13	Municipalities and LTOs, with Wesgro Tourism	Design, then implement
I13	Climate resilience and destination management, including LTO funding	14	DEDAT, with Wesgro Research	Design
I14	Tourism investment pipeline	15	Wesgro investment promotion	Design
I15	Tourism Growth Steerco and three-tier alignment	16, 17	Wesgro CEO's office	Implement
I16	Data-sharing protocol and visitor intelligence	18	Research	Design, then implement
I17	Access and safety escalation agenda	19	Wesgro CEO's office, with DEDAT	Implement
I18	Tourism labour analysis and skills plan	20	DEDAT, with Wesgro Research	Design

Source: Chapter 3 entries; proposed leads for Steerco to confirm. Phase 1 role from the Gantt in section 4.2.

4.2 Sequencing and phases

Three phases run to 2035, and the first is weighted to the moves that change the 2030 constraint: seats, bookability, green-season events and the inclusion pilots.

The phases follow calendar years: Activate from 2027 to 2028, Expand from 2029 to 2031 and Sustain from 2032 to 2035. Each phase ends at a decision gate tied to the Chapter 5 indicators (section 4.7). The first gate, at the end of 2028, falls in Wesgro's FY2028/29, two years before the base case reaches the seat ceiling at its 2030 point (Demand-Side Analysis, Jun 2026, p21).

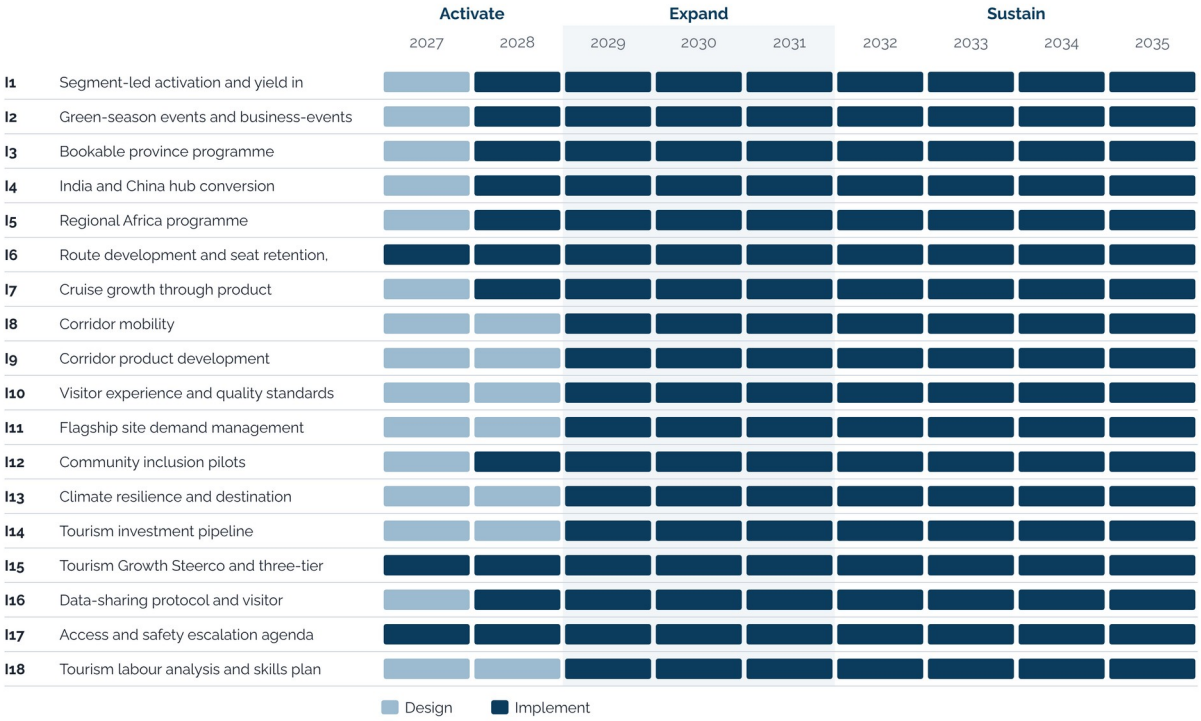


Figure 4.1. Three initiatives start in implementation in 2027, eleven are in implementation by 2028 and all eighteen by 2029.

Source: Letsema, initiative portfolio (sections 4.1 and 4.3). Design means scoping, data, agreements and pilots; implement means delivery at scale.

Phase 1: Activate, 2027 to 2028

Phase 1 works inside Wesgro's mandate and budget and on the levers that move before the airport can. It holds and adds seats on the full routes and builds the air access fund (I6). It publishes the green-season calendar (I2), counts and starts to close the bookability gap (I3) and starts two or three inclusion pilots (I12). Steerco, the data-sharing protocol and the escalation agenda start in the first quarter (I15, I16, I17), because every other initiative reports through them.

The marketing initiatives (I1, I4, I5) and cruise (I7) spend 2027 on design: segment targets, hub-carrier agreements, the Nigeria and Kenya plans and excursion products. Seven initiatives use both years for design (I8 to I11, I13, I14, I18). Their first task is a baseline or a case that no deliverable holds: corridor mobility, product, quality, flagship capacity, climate risk and LTO funding, the investment pipeline and the labour analysis. The gate at the end of 2028 asks three questions. Have seats on the full routes held? Does the bookability baseline exist and is it moving? Has any pilot met its thresholds?

Phase 2: Expand, 2029 to 2031

Phase 2 scales what Phase 1 proved and meets the seat ceiling. Hub conversion, regional Africa and segment marketing run at scale. Corridor mobility and product move from design to delivery, on the Garden Route, the Winelands and the Overberg first. The quality charter is adopted and phased by district, and the investment pipeline reaches financial close on its first projects. The mid-term review in 2030 tests arrivals against the base path when the ceiling binds, and checks that the runway is on its published dates (section 5.6).

Phase 3: Sustain, 2032 to 2035

Phase 3 runs as relief arrives at Cape Town International: the international terminal about 2032 and the runway about 2033 (Infrastructure Report, Jul 2026, p103). The direct India and China route cases built since 2027 go to carriers as capacity frees up, which is the step the accelerated case depends on. Inclusion pilots that met their thresholds scale through channels, climate risk and LTO funding are embedded in municipal planning, and the terminal evaluation in 2035 closes the plan (section 5.6).

4.3 Initiative charters

Each initiative has a one-page charter that a lead can run from and Steerco can hold to account.

Every charter uses the same fields. It states the objective, the focus areas served, the proposed lead and partners and the tier of government. It then sets the actions in each phase, marked Design or Implement, and closes with the dependencies, the funding route, the risks and the indicators it moves. Actions come from the Chapter 3 action tables. Leads are proposals for Steerco to confirm, and rand bands are set in section 4.6.

I1 Segment-led activation and yield in mature markets

Field	Charter
Objective	Raise value per visitor from the mature markets and target every priority market by segment, not by country alone.
Focus areas	1, 5
Proposed lead	Destination Marketing
Partners	Research; trade and OTA partners; SA Tourism
Tier of government	Provincial (Wesgro); national alignment with SA Tourism
Activate, 2027 to 2028	Design (2027): segment targets inside each priority market; a shared segment frame with SA Tourism; destination-specific segment research. Implement (2028): move spend from broad awareness to trade-led conversion; luxury-advisor and high-end operator distribution in the UK, USA, Germany, France and Switzerland.
Expand, 2029 to 2031	Segment campaigns at scale; spend per visitor and length of stay added to Wesgro's own targets; segments built into brand tracking.
Sustain, 2032 to 2035	Segment research refreshed; budget shifted toward the segments and markets with the highest yield.
Dependencies	I6 for seats on the full routes; I16 for spend-per-visitor data; I10 for product quality.
Funding route	Main: Wesgro operating budget. Supporting: private capital. Rand band to be set (section 4.6).
Risks	Carriers on full routes raise fares rather than seats; SA Tourism's institutional weakness limits joint campaigns (Stakeholder Insights Report, Mar 2026, p25).
Indicators	T1-01, T1-02, T1-03; T2-01, T2-07; T3-01 segment targets in Wesgro's annual plan; T3-02 share of market budget in trade-led conversion.

I2 Green-season events and business-events calendar

Field	Charter
Objective	Build an April to September demand spine from business events and flagship weeks, and sell it with the seats.
Focus areas	2
Proposed lead	Convention Bureau
Partners	Destination Marketing; CTICC; City of Cape Town; DEDAT; LTOs
Tier of government	Provincial and local; national for delegate visas
Activate, 2027 to 2028	Design (2027): one event acquisition and calendar strategy across Wesgro, the Convention Bureau, the City and the Province; a way to measure meetings, incentives and exhibitions. Implement (2028): publish the calendar; aim bids at May to September; green-season packages with airlines and trade; cooler-season incentive packages for Indian and Gulf planners.
Expand, 2029 to 2031	Regional conferences in Stellenbosch and George; lifestyle events at CTICC in December and January; flower, fynbos and whale events marketed earlier.
Sustain, 2032 to 2035	Calendar refreshed each year; a standing bid pipeline for green-season dates.
Dependencies	I6 for seats in the trough months; I9 for regional venues; I17 for visas for African delegates.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets. Supporting: private capital. Rand band to be set (section 4.6).
Risks	Weather limits summit and outdoor events (Stakeholder Insights Report, Mar 2026, p35); peak hotel prices deter December and January events (p46).
Indicators	T1-05; T2-02 ICCA meetings, T2-03 May to September seat share; T3-03 calendar published; T3-04 bids for May to September events.

I3 Bookable province programme

Field	Charter
Objective	Make provincial product bookable where travellers book, district by district.
Focus areas	3
Proposed lead	Tourism
Partners	Research; LTOs; district municipalities; OTAs; CapeNature
Tier of government	Provincial and local; national for broadband and payment rules
Activate, 2027 to 2028	Design (2027): a bookability census of provincial product by district. Implement (2028): a digital onboarding drive for small operators and cellars on the West Coast, Route 62 and the Overberg; OTA partnerships with Trip.com, Almosafer and Booking.com; community booking routes with I12.
Expand, 2029 to 2031	Packaged regional itineraries listed on OTAs; CapeNature reservations moved online.
Sustain, 2032 to 2035	Census repeated every two years; listing extended to every route.
Dependencies	I12 for community routes; I16 for the census data; SA Connect rural broadband.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets. Supporting: national programmes and SOEs, private capital. Rand band to be set (section 4.6).
Risks	Rural connectivity and payments; compliance cost for small operators.
Indicators	T2-04 share of operators bookable online, T2-05 CapeNature online share; T3-05 census published; T3-06 operators onboarded.

I4 India and China hub conversion

Field	Charter
Objective	Convert the Indian and Chinese travellers already flying in through hubs, and prepare the direct route case for when runway capacity arrives.
Focus areas	4
Proposed lead	Destination Marketing
Partners	Air Access; hub carriers; OTAs; trade
Tier of government	Provincial; national for visas and route designation
Activate, 2027 to 2028	Design (2027): joint market support with Emirates, Qatar Airways and Ethiopian Airlines; activation plans for Xiaohongshu, Douyin and MakeMyTrip. Implement (2028): in-market activation with Trip.com packages and market-specific itineraries; product readiness with Mandarin and Indian-language guiding and Alipay and WeChat Pay.
Expand, 2029 to 2031	Activation at scale; standing relationships with Indian carriers, China Southern and China Eastern.
Sustain, 2032 to 2035	Direct route cases taken to carriers as runway capacity arrives, with I6.
Dependencies	I6 for route cases; I10 for product readiness; I17 for visas and route designation.
Funding route	Main: Wesgro operating budget. Supporting: private capital. Rand band to be set (section 4.6).
Risks	Visa processing; no Indian aircraft for a direct route before 2030 (MIDAS Aviation Market Assessment, Mar 2026, Indian Market Opportunity).
Indicators	T1-02; T2-06 India and China hub arrivals; T3-07 hub-carrier agreements; T3-08 route cases prepared.

I5 Regional Africa programme

Field	Charter
Objective	Hold the regional volume base and grow Nigeria and Kenya as premium markets.
Focus areas	6
Proposed lead	Destination Marketing
Partners	Air Access; Convention Bureau; regional carriers; trade
Tier of government	Provincial; national for visas and route liberalisation
Activate, 2027 to 2028	Design (2027): Nigeria and Kenya activation plans; Nigeria and Ghana added to the growth model; consumer research for Botswana, Zambia, Ghana and Rwanda. Implement (2028): premium, trade-led activation; capacity cases on the five full regional routes.
Expand, 2029 to 2031	Conferences with leisure extensions; onward packages for regional travellers who stop in Johannesburg.
Sustain, 2032 to 2035	Effort shifted with results; brand seeding in the watch markets.
Dependencies	I6 for regional capacity; I2 for conference demand; I17 for visas.
Funding route	Main: Wesgro operating budget. Supporting: private capital. Rand band to be set (section 4.6).
Risks	Visa friction and budget sensitivity of regional demand (Stakeholder Insights Report, Mar 2026, p45).
Indicators	T1-02; T2-08 African arrivals and spend; T3-09 activation programmes run; T3-10 regional capacity cases made.

I6 Route development and seat retention, with a public-private air access fund

Field	Charter
Objective	Hold and add seats on the full routes until runway relief, and have direct route cases ready when it arrives.
Focus areas	7
Proposed lead	Air Access
Partners	DEDAT; City of Cape Town; ACSA; airlines; private sector
Tier of government	Provincial and local; national for air service agreements; ACSA for airport capacity
Activate, 2027 to 2028	Implement (2027): a seat-retention and frequency programme on the full routes with joint marketing; quarterly runway milestone tracking; a capacity-against-demand model to 2035. Design (2027 to 2028): a public-private air access fund with ring-fenced corridor budgets.
Expand, 2029 to 2031	Fund in operation; frequency and gauge cases on the five full regional routes; growth at George.
Sustain, 2032 to 2035	Direct India and China route cases taken to carriers as runway capacity arrives.
Dependencies	ACSA's programme at Cape Town International; I17 for air service agreements; I4 and I5 for demand.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets, private capital. Supporting: national programmes and SOEs. Rand band to be set (section 4.6).
Risks	Runway relief slips; bilateral agreements stay restrictive (section 4.8).
Indicators	T1-01; T2-09 seats and routes, T2-10 routes above 80% load; T3-11 fund constituted; T3-12 runway milestone reports issued.

I7 Cruise growth through product

Field	Charter
Objective	Grow cruise calls and shore spend through ships that fit, packaged excursions and regional day stops.
Focus areas	8
Proposed lead	Cruise Cape Town
Partners	Transnet National Ports Authority; V&A Waterfront; Mossel Bay municipality; cruise lines
Tier of government	Provincial and local; Transnet for ports
Activate, 2027 to 2028	Design (2027): line targeting for ships that fit the 300m berth; Mossel Bay excursion packages; source and define the 250-call plan. Implement (2028): marketing to expedition and home-porting operators; community product on cruise-operator channels.
Expand, 2029 to 2031	Saldanha Bay only if demand is proven; shore power and wind planning with the ports authority.
Sustain, 2032 to 2035	Longer itineraries and pre- and post-cruise stays.
Dependencies	Berth scheduling by Transnet National Ports Authority; I3 and I12 for bookable shore product.
Funding route	Main: Wesgro operating budget, national programmes and SOEs. Supporting: private capital. Rand band to be set (section 4.6).
Risks	Red Sea reroutes reverse; the 300m ship-length limit (Infrastructure Report, Jul 2026, p110, p112).
Indicators	T2-11 cruise calls and passengers; T3-13 excursion packages listed; T3-14 lines engaged.

I8 Corridor mobility

Field	Charter
Objective	Make the transport that exists usable for visitors and aggregate the demand that makes corridor shuttles viable.
Focus areas	9
Proposed lead	Department of Mobility, with Wesgro Tourism
Partners	City of Cape Town; PRASA; district municipalities; private operators
Tier of government	Provincial, local and national (PRASA)
Activate, 2027 to 2028	Design and pilot (2027 to 2028): a Southern Line visitor product with the City and PRASA; shuttle demand aggregation on the Garden Route and between Cape Town, Darling and the West Coast; transfers sold inside N2 and R62 itineraries.
Expand, 2029 to 2031	Shuttle products in operation; Central Line recovery, MyCiTi Phase 2 and integrated ticketing.
Sustain, 2032 to 2035	A decision on Cape Town to George rapid rail; the last mile to Cape Point.
Dependencies	PRASA and the City of Cape Town; the national rule on bank-card payments on the George bus; I9 for itineraries.
Funding route	Main: provincial and municipal budgets, national programmes and SOEs. Supporting: Wesgro operating budget, private capital. Rand band to be set (section 4.6).
Risks	Rail safety and reliability; shuttle viability at low volumes.
Indicators	T1-06; T2-12 accessibility score, T2-13 corridor transfer products; T3-15 Southern Line product launched; T3-16 shuttle products bookable.

I9 Corridor product development

Field	Charter
Objective	Turn assets outside the Metro into bookable multi-day itineraries, starting with the corridors closest to ready.
Focus areas	10
Proposed lead	Tourism
Partners	LTOs; district municipalities; CapeNature; SANParks; private investors
Tier of government	Provincial and local; national for SANParks precincts and broadband
Activate, 2027 to 2028	Design (2027 to 2028): itineraries for the six touring routes; a plan to activate cold-zone assets; regional conference offers in Stellenbosch and George.
Expand, 2029 to 2031	Delivery on the Garden Route, the Cape Winelands and the Overberg first, then Route 62 and the West Coast.
Sustain, 2032 to 2035	Accommodation and service depth in secondary towns; refreshed flagship product.
Dependencies	I3 for bookability; I8 for transfers; I14 for capital.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets, private capital. Supporting: national programmes and SOEs. Rand band to be set (section 4.6).
Risks	No committed capital for product (Infrastructure Report, Jul 2026, p54, p76); operator capacity.
Indicators	T1-06; T2-14 readiness by district; T3-17 multi-day itineraries listed; T3-18 cold-zone assets activated.

I10 Visitor experience and quality standards

Field	Charter
Objective	Adopt a provincial quality charter, phased by district, and prepare the province for growth-market visitors.
Focus areas	11
Proposed lead	DEDAT, with Wesgro Tourism
Partners	Industry bodies; CATHSSETA; attraction operators
Tier of government	Provincial; industry
Activate, 2027 to 2028	Design (2027 to 2028): a charter with certification visible on booking platforms; support for SMMEs to comply; readiness standards for language, payments and food.
Expand, 2029 to 2031	Charter adopted and phased by district; investment case for mid-scale hotels with I14.
Sustain, 2032 to 2035	Charter embedded in grading; measurement repeated.
Dependencies	I14 for mid-scale capital; I18 for skills; I3 for visibility on platforms.
Funding route	Main: provincial and municipal budgets. Supporting: Wesgro operating budget, private capital. Rand band to be set (section 4.6).
Risks	Compliance burden on small businesses; skills shortages.
Indicators	T2-15 routes rated Ready; T3-19 charter adopted; T3-20 businesses certified.

I11 Flagship site demand management

Field	Charter
Objective	Manage visitor flows at the flagship nature sites and steer visitors to under-marketed reserves.
Focus areas	12
Proposed lead	Site operators, with Wesgro Research
Partners	SANParks; Table Mountain Aerial Cableway; CapeNature; Robben Island Museum; City of Cape Town
Tier of government	National (SANParks), provincial (CapeNature) and site operators
Activate, 2027 to 2028	Design (2027 to 2028): a baseline of visitor counts and capacity for five flagship sites; marketing of reserves and the Southern Line as alternatives.
Expand, 2029 to 2031	Digital flow management and tiered pricing at the Cableway, Boulders and Cape Point; a visitor management plan for Table Mountain National Park and Boulders.
Sustain, 2032 to 2035	Yield measures for nature product; climate-resilient asset formats.
Dependencies	I8 for the Southern Line; I16 for data; I13 for climate risk.
Funding route	Main: national programmes and SOEs, private capital. Supporting: Wesgro operating budget, provincial and municipal budgets. Rand band to be set (section 4.6).
Risks	Operators do not share data; mandates limit pricing (Stakeholder Insights Report, Mar 2026, p44).
Indicators	T2-16 peak Cableway queue; T3-21 flagship baseline published; T3-22 flow tools in place.

I12 Community inclusion pilots

Field	Charter
Objective	Test the Inclusion Plan's model in two or three communities: a seller with a stake, a link to existing demand and gates before any investment.
Focus areas	13
Proposed lead	Municipalities and LTOs, with Wesgro Tourism
Partners	Municipalities; LTOs; community sellers; SAPS
Tier of government	Local and provincial; national for safety (SAPS)
Activate, 2027 to 2028	Design (2027): pilots chosen on readiness; agreement on who funds a seller with a stake in each; safety plans. Implement (2028): one live booking route per pilot; a fixed-date test; product placed in Wesgro's itineraries and calendars.
Expand, 2029 to 2031	Pilots that meet their thresholds scale; covenants on public assets; links to tourism procurement.
Sustain, 2032 to 2035	Extension to more shortlisted communities through channels.
Dependencies	I3 for booking routes; I17 for safety; municipal assets.
Funding route	Main: provincial and municipal budgets. Supporting: Wesgro operating budget, national programmes and SOEs, private capital. Rand band to be set (section 4.6).
Risks	Safety; the selling body is not sustained; capital ahead of demand (SME and Community Inclusion Plan, Sep 2026, p11).
Indicators	T1-07; T2-17 communities with a live booking route; T3-23 pilots selected; T3-24 fixed-date tests held.

I13 Climate resilience and destination management, including LTO funding

Field	Charter
Objective	Track and plan for climate losses, and give local tourism bodies stable funding with a development mandate.
Focus areas	14
Proposed lead	DEDAT, with Wesgro Research
Partners	Municipalities; district municipalities; CapeNature; site operators
Tier of government	Provincial and local; national for Treasury Circular 131
Activate, 2027 to 2028	Design (2027 to 2028): a climate and weather risk register for sites and routes; an LTO funding model in response to Circular 131.
Expand, 2029 to 2031	Funding agreements signed; sustainability checks in the quality charter; itineraries routed around closures.
Sustain, 2032 to 2035	Climate risk and LTO funding embedded in IDPs with reporting.
Dependencies	National Treasury on Circular 131; I10 for the charter.
Funding route	Main: provincial and municipal budgets. Supporting: Wesgro operating budget, national programmes and SOEs, private capital. Rand band to be set (section 4.6).
Risks	Circular 131 unresolved; further climate events (section 4.8).
Indicators	T2-18 LTOs with a funding agreement, T2-19 weather losses at flagship sites; T3-25 risk register published; T3-26 LTO funding model agreed.

I14 Tourism investment pipeline

Field	Charter
Objective	Build a scored pipeline of tourism investments from the gap-closure tables and take it to investors.
Focus areas	15
Proposed lead	Wesgro investment promotion
Partners	DEDAT; Tourism; private investors; municipalities
Tier of government	Provincial and local; private
Activate, 2027 to 2028	Design (2027 to 2028): a pipeline from the gap tables, scored for return, jobs and inclusion; return projections for the SLA; investment cases for mid-scale and conference hotels and for accommodation at De Hoop and on Route 62.
Expand, 2029 to 2031	Investor engagement; first projects at financial close; a tourism levy and blended finance tested with DEDAT.
Sustain, 2032 to 2035	Pipeline refreshed each year; covenants on public assets.
Dependencies	I9 and I10 for product and quality; I6 for the air access fund.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets, private capital. Rand band to be set (section 4.6).
Risks	Capital ahead of demand; tight fiscal space (Stakeholder Insights Report, Mar 2026, p25).
Indicators	T2-20 projects at financial close; T3-27 investment cases prepared; T3-28 investor engagements.

I15 Tourism Growth Steerco and three-tier alignment

Field	Charter
Objective	Give the province one forum, one shared agenda with clear decision rights and one joint plan with industry.
Focus areas	16, 17
Proposed lead	Wesgro CEO's office
Partners	DEDAT; Cape Town Tourism; City of Cape Town; district municipalities; industry bodies
Tier of government	All three tiers and industry
Activate, 2027 to 2028	Implement (2027): Steerco constituted with terms of reference; a decision-rights map by tier from the Diagnostic's tier table; JAMS adopted as the consultation channel; sector councils designed; the demand-side engagement round with the trade.
Expand, 2029 to 2031	A joint industry plan agreed and reviewed each year; sector councils running; regional forums carrying a development agenda.
Sustain, 2032 to 2035	Steerco embedded as the standing governance of the plan; the programme office hands over to the line units by the end of 2031.
Dependencies	DEDAT and Cape Town Tourism as standing members; I17 for the national asks; I16 for the scorecard.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets. Rand band to be set (section 4.6).
Risks	Misalignment between public institutions and industry bodies persists (Stakeholder Insights Report, Mar 2026, p25); SA Tourism's institutional weakness.
Indicators	T2-21 escalation items answered, T2-22 partners in the joint plan; T3-29 Steerco meetings held each quarter; T3-30 joint industry plan agreed.

I16 Data-sharing protocol and visitor intelligence

Field	Charter
Objective	Agree data-sharing terms with every data holder and run one indicator register and dashboard.
Focus areas	18
Proposed lead	Research
Partners	Stats SA; SA Tourism; ACSA; Cape Town Tourism; booking platforms
Tier of government	Provincial; national for the jobs methodology and the tourism satellite account
Activate, 2027 to 2028	Design (2027): data-sharing terms with ACSA, SA Tourism, Stats SA, Cape Town Tourism, site operators and booking platforms; the indicator register. Implement (2028): dashboard live with automated arrivals, seats and cruise feeds; quarterly digital tracking; measurement of meetings, incentives and exhibitions.
Expand, 2029 to 2031	District arrivals and spend baseline; annual brand research; Nigeria and Ghana in the growth model.
Sustain, 2032 to 2035	One reconciled arrivals series; the register refreshed each year.
Dependencies	Agreement from each data holder; the Department of Tourism's methodology; I15 for the forum.
Funding route	Main: Wesgro operating budget. Supporting: provincial and municipal budgets, national programmes and SOEs, private capital. Rand band to be set (section 4.6).
Risks	Data holders do not share; national data lag (Stakeholder Insights Report, Mar 2026, p30, p37).
Indicators	T2-23 automated data feeds; T3-31 data-sharing agreements signed; T3-32 dashboard live.

I17 Access and safety escalation agenda

Field	Charter
Objective	Turn the national deficits into a standing agenda of asks, each with an owner, a decision and a date, backed by evidence.
Focus areas	19
Proposed lead	Wesgro CEO's office, with DEDAT
Partners	Home Affairs; Department of Transport; SAPS; ACSA; SA Tourism
Tier of government	National (Home Affairs, Transport, SAPS, ACSA, PRASA); provincial for safety programmes; local for basic services
Activate, 2027 to 2028	Implement (2027): the first agenda tabled at Steerco: visa categories and processing for China, India, the Middle East and Africa; air service agreements and the US carrier cap; immigration throughput at Cape Town International; station security. Evidence built market by market.
Expand, 2029 to 2031	Responses logged and followed up each quarter; tourism safety units and programmes with the Western Cape Government; safety compacts in pilot communities.
Sustain, 2032 to 2035	Asks updated as airport relief arrives; direct route designations pursued with the national tier.
Dependencies	I15 for the forum; I16 for evidence; I4 to I6 for the market case.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets. Rand band to be set (section 4.6).
Risks	National asks go unanswered; safety incidents (section 4.8).
Indicators	T2-24 visa processing time, T2-21 items answered; T3-33 agenda tabled; T3-34 responses logged.

I18 Tourism labour analysis and skills plan

Field	Charter
Objective	Fix a provincial tourism employment baseline, test the 300,000 ambition and set a skills plan from the result.
Focus areas	20
Proposed lead	DEDAT, with Wesgro Research
Partners	CATHSSETA; industry bodies; training providers
Tier of government	Provincial; national for the jobs methodology and sector training
Activate, 2027 to 2028	Design (2027 to 2028): the labour analysis commissioned; the Pero 2025 tourism employment table extracted; the method note for the jobs ratio obtained; a workforce strand built into the quality charter.
Expand, 2029 to 2031	Skills plan adopted; training partnerships around reserves and in pilot communities; the jobs indicator moved from the ratio to a provincial measure.
Sustain, 2032 to 2035	Labour analysis refreshed for the terminal evaluation.
Dependencies	I10 for the quality charter; I16 for data; the Department of Tourism's methodology.
Funding route	Main: Wesgro operating budget, provincial and municipal budgets. Supporting: national programmes and SOEs, private capital. Rand band to be set (section 4.6).
Risks	No provincial methodology is approved; skills shortages cap service quality.
Indicators	T1-04; T2-25 labour analysis published; T3-35 analysis published; T3-36 skills plan adopted.

4.4 Roles and accountabilities

Wesgro is accountable for twelve initiatives and does part of the work in all eighteen; for the other six, the accountable lead sits with another tier, and the plan names it.

The matrix below assigns each initiative to the four roles: responsible (R) for doing the work, accountable (A) for the result, consulted (C) before decisions and informed (I) of progress. Where Wesgro is accountable and does the work itself, the cell reads A/R. Assignments are proposals for Steerco to confirm, built from the actions in Chapter 3.

Table 4.3. Wesgro is accountable for twelve initiatives; provincial departments, municipalities or site operators are accountable for six, and SOEs or national departments do part of the work in four.

Code	Initiative	Wesgro	Province	City, CTT	Districts, LTOs	SOEs	SAT	National	Industry, sites
I1	Segment-led activation and yield in mature markets	A/R	C	I	I	-	C	-	C
I2	Green-season events and business-events calendar	A/R	C	R	R	-	I	-	C
I3	Bookable province programme	A/R	C	C	R	-	-	I	C
I4	India and China hub conversion	A/R	I	I	-	C	C	C	C
I5	Regional Africa programme	A/R	I	I	-	C	C	C	C
I6	Route development and seat retention, with a public-private air access fund	A/R	R	R	-	C	I	C	C
I7	Cruise growth through product	A/R	I	C	C	R	-	-	C
I8	Corridor mobility	R	A	R	R	R	-	C	C
I9	Corridor product development	A/R	C	C	R	-	-	C	C
I10	Visitor experience and quality standards	R	A	C	C	-	-	-	R
I11	Flagship site demand management	R	C	C	C	-	-	C	A
I12	Community inclusion pilots	R	C	R	A	-	-	C	C
I13	Climate resilience and destination management, including LTO funding	R	A	C	R	-	-	C	R
I14	Tourism investment pipeline	A/R	R	C	C	C	-	-	C
I15	Tourism Growth Steerco and three-tier alignment	A/R	R	R	R	C	C	C	R
I16	Data-sharing protocol and visitor intelligence	A/R	C	R	C	R	R	R	C
I17	Access and safety escalation agenda	A/R	R	C	C	C	C	R	C
I18	Tourism labour analysis and skills plan	R	A	C	C	-	-	C	R

Source: Letsema, from the Chapter 3 action tables; proposed for Steerco to confirm. Province: DEDAT and the Department of Mobility. SOEs: ACSA, Transnet and PRASA. National: Home Affairs, Transport, National Treasury and SAPS. Industry: industry bodies, airlines, CapeNature, SANParks and attraction operators.

National government and the state-owned entities

Four levers sit outside the province and cannot be bought or marketed into place. Route rights and visas sit with the national tier (Current State Diagnostic, Dec 2025, p58), the airport and port capital programmes with

national SOEs (Infrastructure Report, Jul 2026, p103, p112) and policing with SAPS. The plan treats them as an escalation agenda (I17), carried by Steerco through DEDAT to the national departments and SOEs. Each item is stated as a decision, an owner and a date the province is asking for. Wesgro's own route work (I6) runs inside the existing agreements meanwhile.

Provincial government

DEDAT is a standing member of Steerco and the accountable lead where the lever is policy or funding rather than promotion: quality standards (I10), LTO funding and climate risk (I13) and the labour analysis (I18). The Department of Mobility leads the transport half of corridor mobility (I8). Wesgro's units lead the demand, access, product and data initiatives and report through the programme office.

District and local government

Municipalities and LTOs hold the assets, the selling bodies and the visitor services that the regional and inclusion initiatives depend on. They lead the community selling bodies in the pilots (I12), attach covenants to public assets (I12, I14) and carry the route and product work in their districts (I3, I9). The City of Cape Town and Cape Town Tourism are partners on events, mobility and data (I2, I8, I16) and sit on Steerco.

The private sector and site operators

Airlines decide frequency and gauge, hotel investors decide the mid-scale tier and attraction operators manage their own capacity. The plan gives them the evidence and the demand case. It asks for the decisions it cannot make for them: seats on full routes (I6), investment in secondary nodes (I14) and visitor-flow management at flagship sites, where the operators are accountable (I11).

4.5 Tactical wins for the first 24 months

Twelve actions can start by mid-2028 inside Wesgro's current mandate, and each one opens a baseline, a seat or a booking path that a later initiative needs.

The list is weighted the way Phase 1 is: seats, bookability, the green season, inclusion pilots and the data the rest of the plan reports on. Start dates are proposals in half-years. No action needs new capital; the funding route column says where the money comes from.

Table 4.4. Twelve actions for the first 24 months use existing mandates and budgets and open the baselines and booking paths the later initiatives need.

Action	Initiative	Proposed owner	Start	Funding route	What it opens
Hold winter seats with demand: joint green-season marketing with carriers on the full routes	I6, I2	Air Access	2027 H1	Wesgro operating	Seats kept in May to September, when carriers cut first
Publish a green-season events calendar and aim bids at May to September	I2	Convention Bureau	2027 H1	Wesgro operating	A demand spine for the trough months
Track the runway programme quarterly and commission a capacity-against-demand model to 2035	I6	Air Access	2027 H1	Wesgro operating	Early warning on the binding constraint
Constitute Steerco with terms of reference and table the first escalation agenda	I15, I17	Wesgro CEO's office	2027 H1	Wesgro operating	One forum and one route to national decisions
Agree the data-sharing protocol with ACSA, SA Tourism, Stats SA and Cape Town Tourism	I16	Research	2027 H1	Wesgro operating	The feeds the scorecard needs
Run a bookability census of provincial product by district	I3	Research	2027 H1	Wesgro operating	The baseline for the bookability indicator
Request visitor counts and capacity from the five flagship sites	I11	Research	2027 H1	Wesgro operating	The flagship capacity baseline
Commission the tourism labour analysis behind the jobs ambition	I18	DEDAT, with Wesgro Research	2027 H1	Wesgro and DEDAT operating	A tested jobs target
Package the Garden Route and Route 62 with a shuttle transfer sold inside the itinerary	I8, I9	Tourism	2027 H2	Wesgro operating; operators	Car-free multi-day trips beyond the Metro
Package the Southern Line as a visitor product with the City and PRASA	I8	Tourism	2027 H2	Wesgro operating; City	A scenic rail route to Boulders and Simon's Town
Choose two or three pilot communities and agree with municipalities and LTOs who funds a seller with a stake in each	I12	Tourism	2027 H2	Municipal and LTO budgets	The first test of the inclusion model
Give each pilot community one live booking route before any promotion	I12, I3	LTOs, with Tourism	2028 H1	Municipal and LTO budgets	Community product that can be bought

Source: Letsema, from the Chapter 3 action tables and the initiative charters (section 4.3). Owners and start dates are proposals for Steerco to confirm.

4.6 Funding and investment

Most of the plan runs on budgets that already exist; the capital it needs sits with ACSA, PRASA, Transnet and private investors, and none of it has been costed yet.

No deliverable costs any initiative. The Inception Report scoped an investment opportunity framework with return scoring, but no separate output was delivered (Inception Report, Nov 2025, p18, p20), and stakeholders describe Western Cape tourism funding as materially below peer destinations without giving a figure (Stakeholder Insights Report, Mar 2026, p25). This section therefore sets the funding route for each initiative and leaves the rand bands to be set with Wesgro Finance and DEDAT [cost band per initiative and phase: Wesgro Finance and DEDAT to set before Steerco signs off the plan].

Table 4.5. Thirteen initiatives draw mainly on Wesgro's operating budget, and four need private capital as a main source.

Code	Initiative	Wesgro operating	Provincial and municipal	National and SOE	Private capital
I1	Segment-led activation and yield in mature markets	●	-	-	O
I2	Green-season events and business-events calendar	●	●	-	O
I3	Bookable province programme	●	●	O	O
I4	India and China hub conversion	●	-	-	O
I5	Regional Africa programme	●	-	-	O
I6	Route development and seat retention, with a public-private air access fund	●	●	O	●
I7	Cruise growth through product	●	-	●	O
I8	Corridor mobility	O	●	●	O
I9	Corridor product development	●	●	O	●
I10	Visitor experience and quality standards	O	●	-	O
I11	Flagship site demand management	O	O	●	●
I12	Community inclusion pilots	O	●	O	O
I13	Climate resilience and destination management, including LTO funding	O	●	O	O
I14	Tourism investment pipeline	●	●	-	●
I15	Tourism Growth Steerco and three-tier alignment	●	●	-	-
I16	Data-sharing protocol and visitor intelligence	●	O	O	O
I17	Access and safety escalation agenda	●	●	-	-
I18	Tourism labour analysis and skills plan	●	●	O	O

Source: Letsema, from the initiative charters (section 4.3). ● main source; O supporting source; – none expected. Rand values are not estimated.

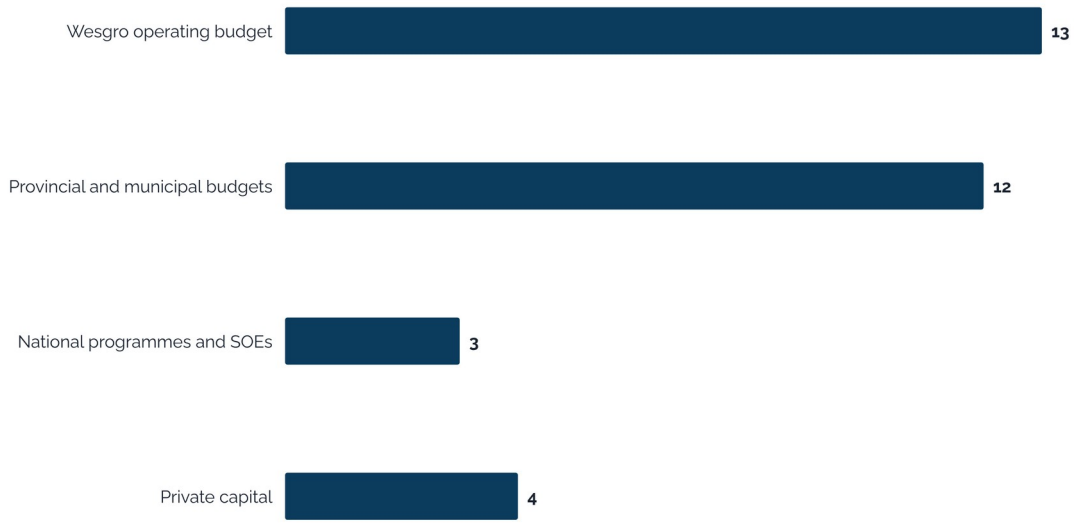


Figure 4.2. Wesgro's operating budget is the main source for most initiatives, while private capital is the main source for the capital-heavy ones.

Source: Letsema, count of initiatives by main funding source from the table above. An initiative can have more than one main source.

Crowding in capital. The rule for capital is the Inclusion Plan's: invest after demand is shown, and attach a maintenance and marketing covenant to any public asset (SME and Community Inclusion Plan, Sep 2026, p15, p31, p32). Wesgro's investment promotion work builds the tourism pipeline from the Infrastructure Report's gap-closure tables, where every district lists tourism gaps with no committed capital (I14; Infrastructure Report, Jul 2026, p32 to p87). The air access fund draws public and private money on the Chilean model (I6; Global Benchmarking Report, Mar 2026, p28).

What the SLA asks and what is still to do. The SLA asks for return projections on infrastructure priorities (clause 1.1.8.3) [clause wording to be checked against the signed Annexure B]. Those need costed projects, and the only costed items in hand are the airport, rail and port programmes the province does not fund. The return case is therefore an output of I14 in Phase 1, built project by project as the pipeline forms.

4.7 Delivery governance

One Steerco, one programme office and four fixed decision points keep eighteen initiatives and three tiers of government on one plan.

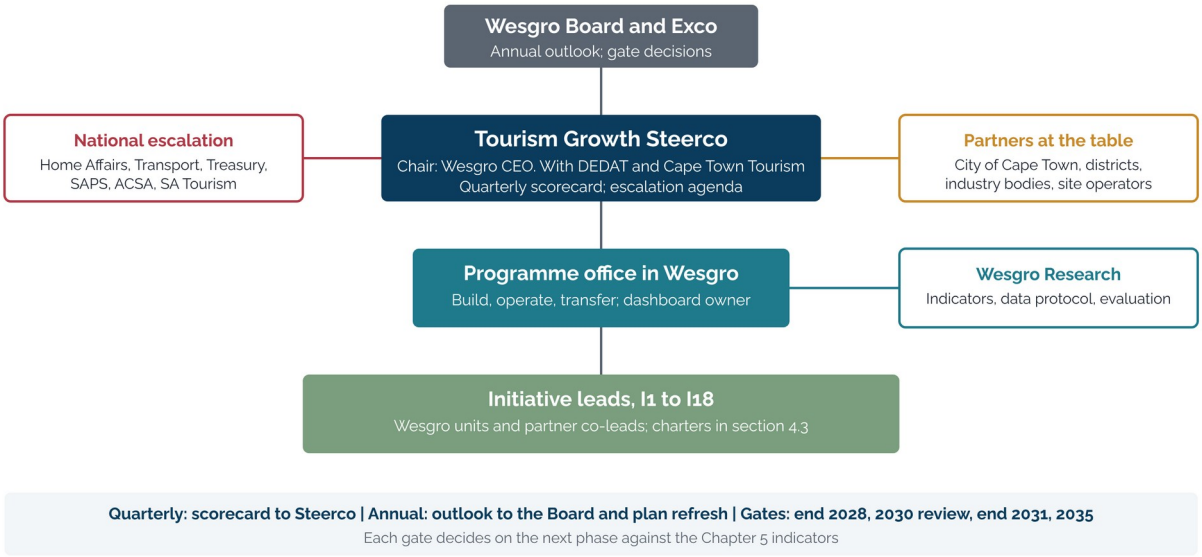


Figure 4.3. Steerco sits between the Board and the initiative leads, with a route to national government on one side and the partners on the other.

Source: Letsema, proposed delivery governance.

Steerco. A Tourism Growth Steerco chaired at Wesgro CEO level, with DEDAT and Cape Town Tourism as standing members and the City of Cape Town, the district municipalities and the industry bodies at the table. It receives the quarterly scorecard, clears cross-initiative issues, holds the escalation agenda and recommends gate decisions to the Board. Stakeholders asked for this kind of alignment directly: mobility responsibilities alone are split across three tiers of government (Stakeholder Insights Report, Mar 2026, p23).

Programme office. A small office inside Wesgro runs the plan on a build, operate and transfer basis. It builds the charters, the dashboard and the reporting calendar in Phase 1, runs them through Phase 2 and hands them to the line units by the end of 2031. It owns the scorecard and the dashboard, and Wesgro Research owns the indicator definitions and the data protocol (I16).

Cadence. Initiative leads report monthly to the programme office, Steerco meets quarterly and the Board receives an annual outlook, which also anchors the Unlocking Tourism business outlook event. The plan is refreshed each year against the indicators and the gate decisions.

Table 4.6. Four decision points test the plan against its indicators, and each one decides what the next phase funds.

Gate	When	What it tests	What it decides
Gate 1	End 2028	Seats on full routes held or added (T2-09, T2-10); bookability baseline published and moving (T2-04); pilots against thresholds (T2-17); data protocol live (T2-23)	Move to Expand; scale or stop each pilot; confirm route cases for India and China
Mid-term review	2030	Arrivals against the base path at the seat ceiling (T1-01); runway on its published dates; green-season share (T1-05)	Re-sequence Phase 2 if the ceiling binds early or relief slips

Gate	When	What it tests	What it decides
Gate 2	End 2031	Spend and spread (T1-03, T1-06); corridor readiness (T2-14); investment at financial close (T2-20)	Commit Phase 3 funding; take direct route cases to carriers
Terminal evaluation	2035	All Tier 1 indicators against the base and accelerated paths	Close the plan and set the next one

Source: Letsema, proposed gates; indicator codes from section 5.2.

4.8 Risks and dependencies

Six of the ten material risks sit outside Wesgro's control, so the mitigation for most of them is early warning and a route to the tier that can act.

Likelihood and impact are Letsema's assessment on a three-point scale, from the evidence cited in each row. Steerco reviews the register each quarter and the owner reports on any risk rated high on both.

Table 4.7. Ten risks could move the plan off its path, and the one rated high on both measures concerns the national air regime.

Risk	Evidence	Likelihood	Impact	Mitigation	Owner
Runway relief at Cape Town International slips past about 2033	IR p103, p109	Medium	High	Quarterly milestone tracking; frequency and gauge on full routes; George as second gateway (I6)	Air Access; ACSA
Bilateral air agreements and the US carrier cap stay restrictive	SIR p24; Inc p8	High	High	Escalation agenda with stated asks (I17); route work inside existing rights (I6)	Steerco; DEDAT
Visa processing for China, India and African markets does not improve	SIR p36, p45; Diag p34	Medium	High	Escalation agenda; processing time tracked as T2-24 (I17)	Steerco
Safety incidents or perception deter visitors	Diag p55; SCIP p27, p30	Medium	High	Safety gates before any pilot launch (I12); escalation to SAPS (I17)	Tourism; Steerco
Climate events close sites and routes	SCIP p24; SIR p33, p43	High	Medium	Climate risk register; itineraries routed around closures (I13)	Research; DEDAT
Water and power supply fail in peak season	Diag p38, p43; IR p31	Medium	Medium	Escalation of utility risks; off-grid power at remote sites (I13, I17)	DEDAT; site operators
LTO funding collapses under Treasury Circular 131	SIR p25, p39	High	Medium	Stable funding agreements with a development mandate (I13)	DEDAT; municipalities
Data holders do not share data	SIR p37; Diag p57	Medium	Medium	Data-sharing protocol with each holder (I16)	Research
Cruise growth reverses as Red Sea reroutes end	IR p112	Medium	Low	Diversify lines and add Mossel Bay day stops (I7)	Cruise Cape Town
Skills shortages cap service quality	SIR p43; Inc p8	Medium	Medium	Labour analysis and skills plan (I18); quality charter (I10)	Research; DEDAT

Source: Letsema assessment. Evidence: Current State Diagnostic, Dec 2025 (Diag); Stakeholder Insights Report, Mar 2026 (SIR); Infrastructure Report, Jul 2026 (IR); SME and Community Inclusion Plan, Sep 2026 (SCIP); Inception Report, Nov 2025 (Inc).

Monitoring and evaluation framework

5.1 Results chain

Every initiative is measured at three levels: what it produces, what changes because of it and what that adds to the 2035 case.

The framework is the written form of the M&E toolkit the SLA requires (clauses 1.1.4 and 1.1.10). It sets indicators, baselines and targets for arrivals, spend, jobs, airlift, cruise and SMME inclusion, with the tools to track them [clause wording to be checked against the signed Annexure B]. The Inception Report adds geographic spread and asks for definitions, sources, frequency, owners and governance for each indicator (Inception Report, Nov 2025, p23).

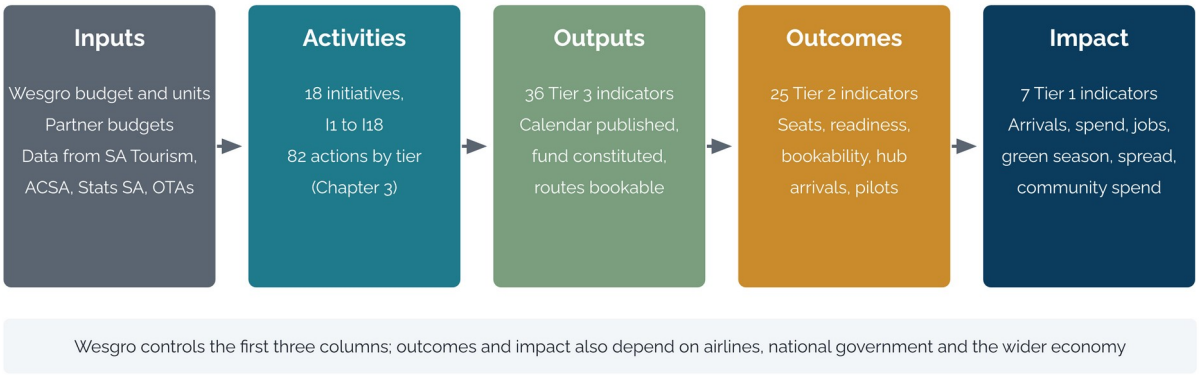


Figure 5.1. Initiatives produce outputs Wesgro controls, which move outcomes Wesgro shares with partners, which add up to the 2035 impact.

Source: Letsema, results chain for the plan.

The three tables below give the chain for each pillar. Tier 3 output indicators come from the initiative charters, Tier 2 outcome indicators from the focus areas and Tier 1 impact indicators from the growth case.

Table 5.1. Pillar 1 initiatives move arrivals, market mix, spend and the green-season share.

Initiative (activity)	Outputs (Tier 3)	Outcomes (Tier 2)	Impact (Tier 1)
I1 Segment-led activation and yield	T3-01, T3-02 segment targets set; spend moved to conversion	T2-01 segment home-market arrivals; T2-07 mature-market spend per visitor	T1-01, T1-02, T1-03
I2 Green-season events calendar	T3-03, T3-04 calendar published; green-season bids	T2-02 ICCA meetings; T2-03 May to September seat share	T1-05
I3 Bookable province	T3-05, T3-06 census published; operators onboarded	T2-04 operators bookable online; T2-05 CapeNature online share	T1-06
I4 India and China hub conversion	T3-07, T3-08 carrier agreements; route cases	T2-06 India and China hub arrivals	T1-01, T1-02
I5 Regional Africa	T3-09, T3-10 activation run; capacity cases	T2-08 African arrivals and spend	T1-02, T1-03

Source: Initiative charters (section 4.3); indicator register (section 5.2).

Table 5.2. Pillar 2 initiatives move seats, cruise volumes and the share of visitors and spend outside the Metro.

Initiative (activity)	Outputs (Tier 3)	Outcomes (Tier 2)	Impact (Tier 1)

Source: Initiative charters (section 4.3); indicator register (section 5.2).

Table 5.3. Pillar 3 initiatives move community spend and jobs, and supply the governance and data every other indicator relies on.

Initiative (activity)	Outputs (Tier 3)	Outcomes (Tier 2)	Impact (Tier 1)
I12 Community inclusion pilots	T3-23, T3-24 pilots selected; tests held	T2-17 communities with a live booking route	T1-07
I13 Climate resilience and LTO funding	T3-25, T3-26 risk register; funding model	T2-18 LTOs funded; T2-19 weather losses	T1-06
I14 Tourism investment pipeline	T3-27, T3-28 cases prepared; investor engagements	T2-20 projects at financial close	T1-03, T1-04
I15 Steerco and three-tier alignment	T3-29, T3-30 quarterly Steerco; joint industry plan	T2-21 escalations resolved; T2-22 partners in the joint plan	All
I16 Data protocol and intelligence	T3-31, T3-32 agreements signed; dashboard live	T2-23 data feeds in the dashboard	All
I17 Access and safety escalation	T3-33, T3-34 agenda tabled; responses logged	T2-24 visa processing time	T1-01, T1-02
I18 Labour analysis and skills plan	T3-35, T3-36 analysis published; skills plan adopted	T2-25 labour analysis published	T1-04

Source: Initiative charters (section 4.3); indicator register (section 5.2).

5.2 Indicator set

Seven impact indicators, twenty-five outcome indicators and thirty-six output indicators measure the plan, each with a definition, a source, an owner and a frequency.

Tier 1 measures the 2035 case and is reported to the Board. Tier 2 measures the focus areas, one or two each, and is reported to Steerco each quarter where the source allows. Tier 3 measures the initiatives' own outputs and is reported by the leads to the programme office each month. The full register, with targets, sits in the toolkit (section 5.7).

Table 5.4. Seven Tier 1 indicators measure arrivals, market mix, spend, jobs, season, spread and community spend.

Code	Indicator	Definition	Source	Frequency	Owner
T1-01	International arrivals	Arrivals, growth-model basis; quarterly proxy: international passenger arrivals at CTIA	SA Tourism; ACSA	Annual; quarterly proxy	Research
T1-02	Arrivals by market group	Arrivals in the mature, hub, regional, acceleration and strategic groups	SA Tourism	Annual	Research
T1-03	Direct foreign spend	Foreign direct spend in the Western Cape, rand	SA Tourism	Annual; quarterly shares	Research
T1-04	Tourism jobs	Jobs supported by international air arrivals, on Wesgro's ratio, until the labour analysis sets a provincial measure	Wesgro ratio; Stats SA TSA	Annual	Research
T1-05	Green-season share	Share of overseas visitor travel in April to September	SA Tourism; Wesgro visitor tracking	Annual	Research
T1-06	Share outside the Metro	Share of arrivals and of spend recorded outside the Cape Metro	SA Tourism provincial data; data protocol	Annual	Research
T1-07	Community share of foreign direct spend	Spend traced to businesses trading inside the 20 shortlisted communities, as a share of foreign direct spend	Pilot records; SA Tourism	Annual	Tourism; Research

Source: Letsema, indicator register; SLA clauses 1.1.4 and 1.1.10; Inception Report, Nov 2025, p22, p23. Baselines and targets in section 5.3.

Table 5.5. Twenty-five Tier 2 indicators give each focus area one or two outcome measures, and seven of them have no baseline yet.

Code	Indicator	Focus area	Baseline	Source
T2-01	Arrivals from the four largest segment home markets (UK, Germany, USA, India)	1	503,277 (2025, computed)	MA p21, p22
T2-02	ICCA association meetings in Cape Town	2	58 (2024)	DSA p37
T2-03	May to September share of international seats at CTIA	2	34.0% (2025, computed)	MIDAS, Seasonality
T2-04	Share of operators bookable online, by district	3	Not in hand; about 40% or more of smaller operators lack online booking (Metro slide, scope not stated)	IR p32
T2-05	CapeNature reservations made online	3	About 70% through the call centre	SIR p42

Code	Indicator	Focus area	Baseline	Source
T2-06	India and China arrivals via hubs	4	India 71,000; China 29,600 (2025)	MIDAS, The Indian Market Opportunity; The Chinese Market Opportunity
T2-07	Spend per visitor, mature markets	5	USA R32,900; UK R26,500; Germany R25,600 (2024)	DSA p14
T2-08	African arrivals and spend	6	323,971 arrivals (2024); R4.2bn spend (2025)	DSA p27, p29
T2-09	International seats and routes at CTIA	7	3,816,797 seats, printed network total (27 routes tabled; year to Nov 2025); 29 routes (2026)	MIDAS, The Capetown Market; Seasonality
T2-10	Routes above 80% load	7	11 of 27 (year to Nov 2025)	MIDAS, Seasonality
T2-11	Cruise calls and passengers	8	79 vessels; 127,178 passengers (2024/25); the Infrastructure Report counts 83 calls (p110)	Diag p37
T2-12	Accessibility score by district	9	Metro 4.7 to Central Karoo 1.0 (2026)	IR p88
T2-13	Corridor transfer products on sale	9	No inter-town tourism shuttle on the Garden Route	IR p90
T2-14	Overall readiness by district	10	Metro 4.5; Garden Route and Winelands 3.4; Overberg 2.7; West Coast 2.5; Central Karoo 1.9	IR p28 to p85
T2-15	Touring routes rated Ready	11	1 of 6 (2026)	IR p30, p40, p51, p62, p73, p84
T2-16	Peak queue at the Cableway	12	Up to three hours up and two down	SIR p36
T2-17	Communities with a live booking route	13	0 of 19 profiled rate Ready on bookability	SCIP p20 to p26, p40 to p51
T2-18	LTOs with a funding agreement	14	Not in hand	SIR p25
T2-19	Weather losses at flagship sites	14	Robben Island roughly R16m a year	SIR p33
T2-20	Tourism projects at financial close	15	None; tourism gaps carry no committed capital	IR p32 to p87
T2-21	Escalation items answered by the national tier	16	No agenda tabled yet	This plan
T2-22	Industry partners signed up to the joint plan	17	No joint plan; 15 of 16 organisations raised collaboration	SIR p20 to p46
T2-23	Automated data feeds in the dashboard	18	None; no dashboard	This plan
T2-24	Visa processing time, priority markets	19	Not in hand	SIR p36, p45
T2-25	Tourism labour analysis published	20	No labour analysis in any deliverable	Inc p4

Source: Chapter 3 evidence tables. MA: Market Assessment Report, May 2026. DSA: Demand-Side Analysis, Jun 2026. IR: Infrastructure Report, Jul 2026. SIR: Stakeholder Insights Report, Mar 2026. SCIP: SME and Community Inclusion Plan, Sep 2026. Diag: Current State Diagnostic, Dec 2025. Inc: Inception Report, Nov 2025. MIDAS: MIDAS Aviation Market Assessment, Mar 2026. Computed values are sums or shares of printed figures.

Table 5.6. Thirty-six Tier 3 output indicators, two per initiative, track what each lead delivers.

Codes	Initiative	Outputs
T3-01, T3-02	I1	Segment targets in Wesgro's annual plan; share of market budget in trade-led conversion
T3-03, T3-04	I2	Green-season calendar published; bids submitted for May to September events
T3-05, T3-06	I3	Bookability census published; operators onboarded to online booking

Codes	Initiative	Outputs
T3-07, T3-08	I4	Joint marketing agreements with hub carriers; India and China route cases prepared
T3-09, T3-10	I5	Activation programmes run in Nigeria and Kenya; regional capacity cases made
T3-11, T3-12	I6	Air access fund constituted; quarterly runway milestone reports issued
T3-13, T3-14	I7	Excursion packages listed; lines engaged on expedition and home-porting
T3-15, T3-16	I8	Southern Line visitor product launched; corridor shuttle products bookable
T3-17, T3-18	I9	Multi-day itineraries listed per route; cold-zone assets activated
T3-19, T3-20	I10	Quality charter adopted; businesses certified
T3-21, T3-22	I11	Flagship baseline published; flow-management tools in place
T3-23, T3-24	I12	Pilot communities selected; fixed-date tests held
T3-25, T3-26	I13	Climate risk register published; LTO funding model agreed
T3-27, T3-28	I14	Investment cases prepared; investor engagements held
T3-29, T3-30	I15	Steerco meetings held each quarter; joint industry plan agreed
T3-31, T3-32	I16	Data-sharing agreements signed; dashboard live
T3-33, T3-34	I17	Escalation agenda tabled; responses logged
T3-35, T3-36	I18	Labour analysis published; skills plan adopted

Source: Initiative charters, section 4.3. Each output has a baseline of zero at the start of 2027.

5.3 Baselines and targets

The arrivals targets come straight from the growth model, the jobs targets from a stated ratio, and the other Tier 1 targets wait for baselines that do not yet exist.

Baselines are fixed at 2025, the growth model's base year, for the growth-model indicators and at FY2024/25 for the airport series, the recovery baseline used in Chapter 1. Targets follow two paths: the base case, which assumes Wesgro's current activity continues with hub carriers adding capacity, and the accelerated case, which adds direct India and China routes and dedicated activation (Demand-Side Analysis, Jun 2026, p19). The model prints the base case for 2028, 2030, 2032, 2034 and 2035, and the other paths for 2035 only. The 2031 base value and the accelerated milestones are computed and marked as such.

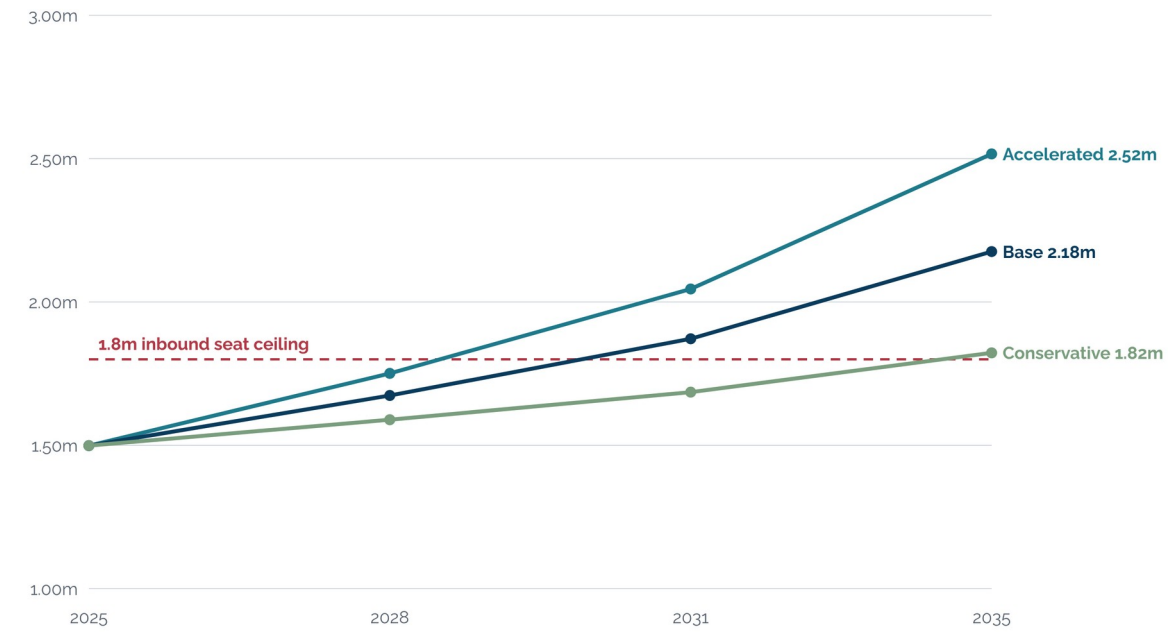


Figure 5.2. Only the accelerated path clears 2.5 million arrivals in 2035, and the base path passes the 1.8m seat ceiling before 2031.

Source: Market Assessment Report, May 2026, p19 (2025 base); Demand-Side Analysis, Jun 2026, p20, p21 (2028 and 2035 points; 1.8m ceiling). The 2031 base value is the geometric mean of the printed 2030 and 2032 points; the accelerated and conservative milestones are computed at a constant rate between the printed 2025 and 2035 values.

Table 5.7. Arrivals and jobs carry targets on both paths; spend carries the working analysis's base path; the other Tier 1 indicators carry dated baselines first.

Indicator	Baseline	2028 base / accelerated	2031 base / accelerated	2035 base / accelerated
T1-01 International arrivals	1,498,829 (2025); CTIA 1.44m (FY24/25)	1,673,855 / 1,750,871*	1,871,637 / *2,045,297*	2,175,778 / 2,516,282
T1-02 Arrivals by market group	Mature 587,287; hubs 427,803; regional 292,514; acceleration 182,815 (2025)	Base path by group, section 2.1	2030: 670,350; 523,523; 343,096; 255,159	766,067; 634,387; 402,812; 358,633 (base); accelerated not split
T1-03 Direct foreign spend	R25.9bn (FY2025)	Not printed	R33.7bn in 2030 (base, modelled)	R40.6bn (base, modelled); accelerated not modelled

Indicator	Baseline	2028 base / accelerated	2031 base / accelerated	2035 base / accelerated
T1-04 Tourism jobs (ratio)	About 30,000 jobs supported (2025)	33,500 / 35,000*	37,400 / 40,900*	43,500 / 50,300*
T1-05 Green-season share	About 35% (2025, provisional; 38.1% normalised); 39% (2024)	Level set at Gate 1	Rising	Rising
T1-06 Share outside the Metro	Not in hand; baseline due in 2027 from the data protocol	Baseline set	Rising	Rising
T1-07 Community share of spend	0.02% to 0.04%; R4m to R10m a year (floor)	Pilots measured	Level set after the pilots	1% (R259m at FY2025 spend) as the reference point

Source: T1-01: Market Assessment Report, May 2026, p19; Demand-Side Analysis, Jun 2026, p11, p20, p21 (computed values marked *). T1-02: Market Assessment Report, May 2026, p20. T1-03: Demand-Side Analysis, Jun 2026, p11 (baseline); Market Assessment Report, May 2026, p24 (modelled base path, working analysis). T1-04: Wesgro's ratio of two jobs per 100 international passengers, applied to T1-01 (computed; public source, see the note below). T1-05: Demand-Side Analysis, Jun 2026, p12; Current State Diagnostic, Dec 2025, p32. T1-07: SME and Community Inclusion Plan, Sep 2026, p5.

Arrivals. The model's 2025 base and the airport series measure different things: tourist arrivals on the model's basis, and international passenger arrivals at Cape Town International. The airport series is the quarterly proxy because ACSA publishes it, and it stood at 1.44m in FY24/25 and 1.57m in FY25/26 (Demand-Side Analysis, Jun 2026, p11). Both are reported, each against its own history.

Jobs. No deliverable carries a provincial tourism employment baseline, and the Pero tourism table could not be retrieved [provincial tourism employment baseline: Wesgro Research to supply from the Pero 2025 or the Stats SA provincial TSA]. The Tier 1 measure is therefore jobs supported by international air arrivals, on Wesgro's own rule of thumb of two jobs for every 100 international passengers, which counts direct, indirect and induced jobs (public source: Wesgro and Cape Town Air Access releases, 2023 to 2024) [methodology note for the ratio: Cape Town Air Access to supply]. Applied to the arrivals paths, it gives about 30,000 jobs in 2025 and adds about 13,500 on the base path and 20,300 on the accelerated path by 2035. It is a ratio-based projection, not a labour-market measure.

The ratio does not reach the 300,000 tourism-linked jobs in the Inception Report's ambition, because it counts only jobs linked to international air arrivals (Inception Report, Nov 2025, p4). The report restates the 300,000 as a total-sector figure for the labour analysis to test (I18). For context, public sources put direct tourism employment at 106,707 in Cape Town in 2024 (City of Cape Town, Economic Value of Tourism, 2025) and 953,981 nationally in 2024 (Stats SA Tourism Satellite Account, provisional, as reported in 2026).

Green season. Plan decision 6 sets the October to March share at about 65% for 2025, provisional, which puts the green season at about 35%. The 2025 month table sums to 104.9%, and once normalised it gives 61.9% and 38.1%, in line with the printed 61% and 39% for 2024 (Demand-Side Analysis, Jun 2026, p12; Current State Diagnostic, Dec 2025, p32). The report recommends the normalised figure as the baseline [Michael to confirm: switch the T1-05 baseline to 38.1%].

Spread and community spend. No deliverable prints district visitor spend, so the share outside the Metro has no baseline until the data protocol delivers one (I16). The community share starts from the Inclusion Plan's traced floor; its 1% is a reference point the plan prints, not a target any party has adopted (SME and Community Inclusion Plan, Sep 2026, p5).

5.4 Data sources and gaps

Arrivals, seats and cruise volumes can be tracked from existing feeds; spread, bookability, jobs and community spend cannot until new data is built or shared.

Stakeholders put data among the top barriers: no approved methodology exists for provincial tourism GDP and jobs (Stakeholder Insights Report, Mar 2026, p37), and no one holds a single view of visitor behaviour (Current State Diagnostic, Dec 2025, p56, p57). The data-sharing protocol under focus area 18 (I16) is the route to closing the gaps below.

Table 5.8. Six sources cover most of the indicators, and each has a named holder the protocol must reach.

Source	Holder	Indicators	Frequency	Status
Departure survey and performance reports	SA Tourism	T1-01 to T1-03, T1-05, T2-07, T2-08	Quarterly and annual	Published; provincial cuts on request
Passenger statistics and schedules	ACSA; OAG	T1-01 proxy, T2-03, T2-09	Monthly	Available; automated feed possible
GDS bookings by route	MIDAS or a data vendor	T2-06, T2-10	Annual	Repeat commission needed
Cruise season economic contribution	Cruise Cape Town (economic contribution study)	T2-11	Each season	Received by Wesgro; study not in this evidence base
Infrastructure readiness scores	Wesgro; Letsema method	T2-12, T2-14, T2-15	Every three years	Re-score in 2029 and 2032
Operator, site and pilot records	LTOs; CapeNature; site operators; pilots	T2-04, T2-05, T2-16, T2-17, T2-19	Annual	New collection under the protocol

Source: Letsema, from the indicator register; data holders in part as listed in Current State Diagnostic, Dec 2025, p56, p57.

Table 5.9. Eleven data gaps stand between the plan and a full baseline, and each has a proposed owner and date.

Gap	Indicator	Proposed owner	Proposed date	Route
District-level visitor arrivals and spend	T1-06	Research	End 2027	SA Tourism cut; protocol
Provincial tourism employment baseline	T1-04	Research	Mid 2027	Pero; Stats SA provincial TSA
Methodology for two jobs per 100 passengers	T1-04	Air Access	Mid 2027	Cape Town Air Access note
Count of bookable products by district	T2-04	Research	End 2027	Bookability census (I3)
Visitor counts and capacity at five flagship sites	T2-16	Research	End 2027	Request to operators (I11)
Meetings, incentives and exhibitions volumes	T2-02	Convention Bureau	End 2028	Venue and DMC returns
LTOs and their municipal funding	T2-18	DEDAT	End 2027	LTO survey
Visa processing times by market	T2-24	Wesgro CEO's office	End 2027	Request to Home Affairs (I17)
Nigeria and Ghana in the growth model	T1-02	Research	Mid 2027	Model update
Source and definition of the 250 cruise-call plan	T2-11	Cruise Cape Town	Mid 2027	Cruise Cape Town
Mid-scale accommodation stock by district	T2-15	Research	End 2028	Supply database or audit

Source: Letsema, from the placeholders in Chapters 3 and 5; owners and dates proposed for Steerco to confirm.

5.5 Tracking mechanism

A quarterly scorecard to Steerco, an annual outlook to the Board and a live dashboard where the sources allow it.

Four principles run the tracking. Automate before collecting by hand: arrivals, seats and cruise volumes come from feeds that already exist. Name one owner for the dashboard (the programme office) and one for the definitions (Wesgro Research). Report every indicator against its own baseline and both paths. Refresh the register each year at the plan review.



Figure 5.3. The scorecard puts the seven impact indicators on one line, then seats and arrivals by month, initiative status and the outcome indicators by pillar.

Source: Letsema, dashboard concept. Illustrative layout; no values shown.

Table 5.10. Monthly, quarterly and annual reporting run on a fixed calendar tied to Steerco and the Board.

Cycle	What is reported	From and to	Format
Monthly	Tier 3 outputs and initiative status; seats and arrivals feeds	Leads to the programme office	Dashboard update
Quarterly	Tier 2 outcomes where available; risks rated high; escalation responses	Programme office to Steerco	Scorecard
Annual	Tier 1 impact against both paths; plan refresh; gate status	Steerco to the Board; public at the business outlook event	Outlook report
At gates	Gate tests in section 4.7	Steerco to the Board	Gate paper

Source: Letsema, proposed reporting calendar.

5.6 Evaluation and learning

Two evaluations bracket the plan: a mid-term review in 2030, when the seat ceiling binds, and a terminal evaluation in 2035.

The mid-term review tests whether the plan is on its path and whether the path still holds. It falls in 2030 because that is when the base case reaches the 1.8 million seat ceiling (Demand-Side Analysis, Jun 2026, p21) and two years before relief at Cape Town International (Infrastructure Report, Jul 2026, p103). The terminal evaluation in 2035 measures the result against both paths and sets up the next plan. Both should be run by a party independent of the programme office.

Table 5.11. Each pillar carries two evaluation questions, one on results and one on the assumptions behind them.

Pillar	Did it work?	Does the logic still hold?
1 Reshape demand	Did arrivals, spend per visitor and the green-season share move with the activation, and in which markets and segments?	Is conversion still the constraint, or has access overtaken it in the growth markets?
2 Transform supply	Did seats, readiness and bookability rise outside the Metro, and did visitors follow?	Did the airport relief arrive on time, and did the second gateways carry the load meanwhile?
3 Build enabling capability	Did the pilots meet their thresholds, and did community spend rise?	Did the national asks get answers, and did the data protocol deliver the baselines?

Source: Letsema, proposed evaluation questions.

Pilots before capital. The inclusion pilots are evaluated before any capital is committed, on the Inclusion Plan's own measures: bookings, visitors and locally retained revenue (SME and Community Inclusion Plan, Sep 2026, p33). A pilot scales only when it meets the thresholds agreed before launch (p32). The same rule applies to any product or asset investment under I9 and I14: test demand, then invest.

Learning into the plan. Findings from each review, gate and pilot go into the annual plan refresh under section 4.7, so the charters, targets and sequence change with the evidence rather than at the end of the plan.

5.7 Toolkit handover

The M&E toolkit turns this chapter into four working files that Wesgro Research owns from handover.

Table 5.12. Four files make up the toolkit, and each has one owner in Wesgro.

File	Contents	Owner
Indicator register	All 68 indicators with definition, unit, source, frequency, owner, baseline and target by year and path	Research
Baseline workbook	The baseline values with page references to the deliverables, and the computed values with their method	Research
Scorecard template	The quarterly Steerco scorecard and the annual Board outlook	Programme office
Dashboard data model	Feeds, refresh frequency and manual-entry forms for the dashboard in section 5.5	Programme office

Source: Letsema; SLA clauses 1.1.10.2 and 1.1.15.3 [clause wording to be checked against the signed Annexure B].

Handover runs through knowledge-transfer sessions with Wesgro Research and the programme office, as the SLA requires (clause 1.1.15). The Excel toolkit itself is outside this report and is listed as an open item [M&E toolkit workbook: Letsema to deliver with the final report].
